


APR01 UPDATED DRAFT
LC609 BRIDGEWATER
PHASING EXPLORATION

LC609 BRIDGEWATER- PHASING ON CURRENT LAYOUT

- PHASE 1 - 5 Weeks
- PHASE 2 - 6 Weeks
- PHASE 3 - 4 Weeks
- PHASE 4 - 4 Weeks (4th Week Dark)

+ SET DOWN - 1 Week

TOTAL WEEKS 20 (19 + 1)

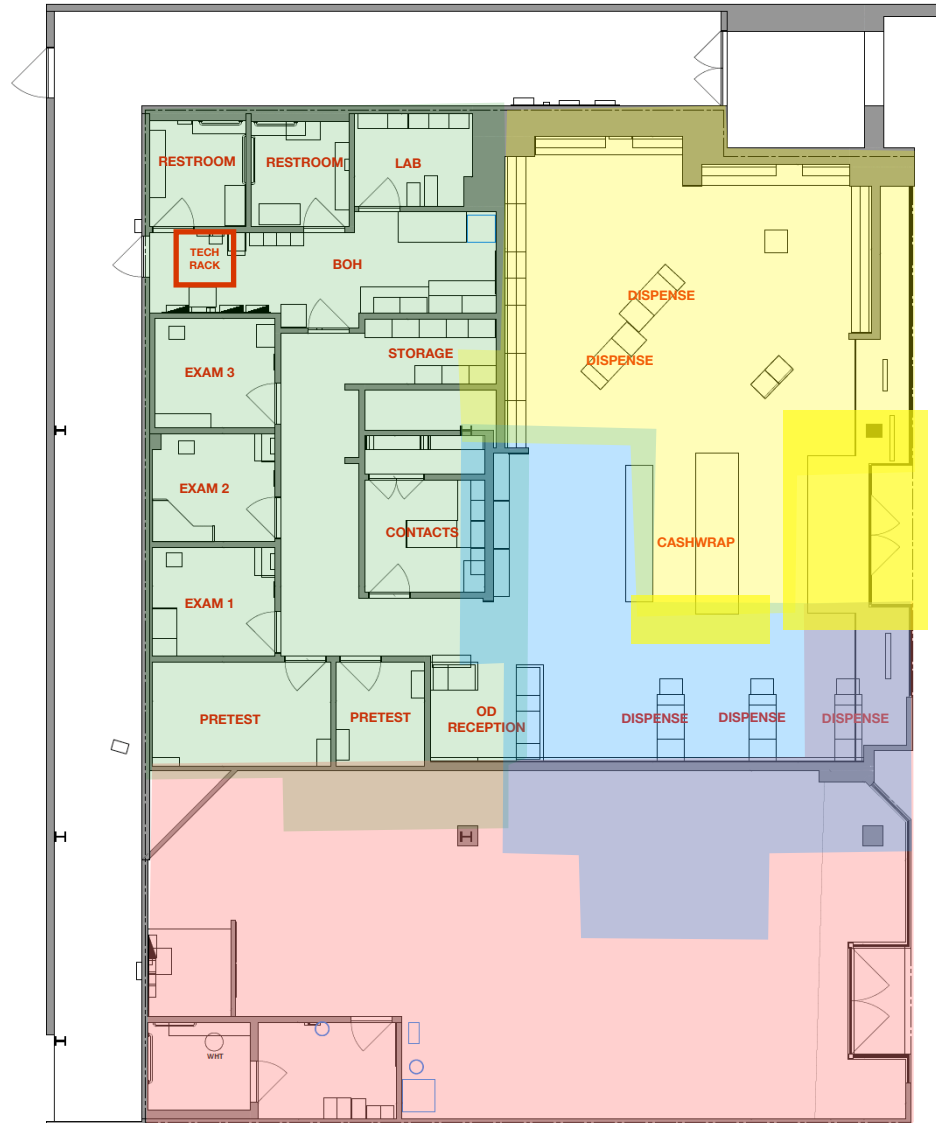


LC609 BRIDGEWATER- PHASING ON FINAL LAYOUT

- PHASE 1 - 5 Weeks
- PHASE 2 - 6 Weeks
- PHASE 3 - 4 Weeks
- PHASE 4 - 4 Weeks (4th Week Dark)

+ SET DOWN - 1 Week

TOTAL WEEKS 20 (19 + 1)

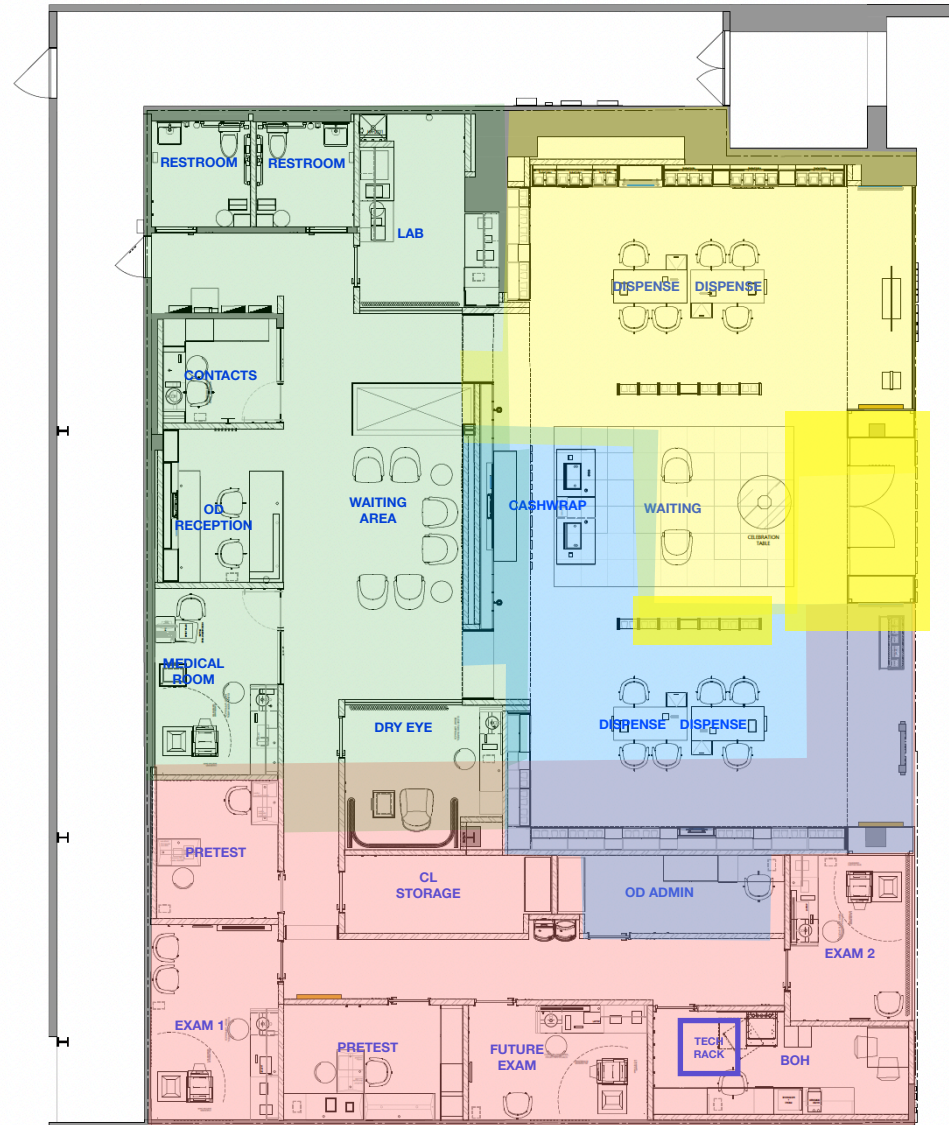

LC609 BRIDGEWATER- CURRENT LAYOUT

- PHASE 1 - 5 Weeks
 - PHASE 2 - 6 Weeks
 - PHASE 3 - 4 Weeks
 - PHASE 4 - 4 Weeks (4th Week Dark)
- + SET DOWN - 1 Week
- TOTAL WEEKS 20 (19 + 1)**



LC609 BRIDGEWATER- PHASE 1 PREP/CONSTRUCTION


- PHASE 1 - 5 Weeks
- PHASE 2 - 6 Weeks
- PHASE 3 - 4 Weeks
- PHASE 4 - 4 Weeks (4th Week Dark)

+ SET DOWN - 1 Week

TOTAL WEEKS 20 (19 + 1)

- DRYWALL BARRICADE
- ONE 8' SLAT PANEL
- 40 ACRYLIC SHELVES 24"L X 6"D EA - A MUST

- 1 DISPENSE STATION RELOCATED TO OTHER SIDE OF STORE
- POWER/DATA A MUST

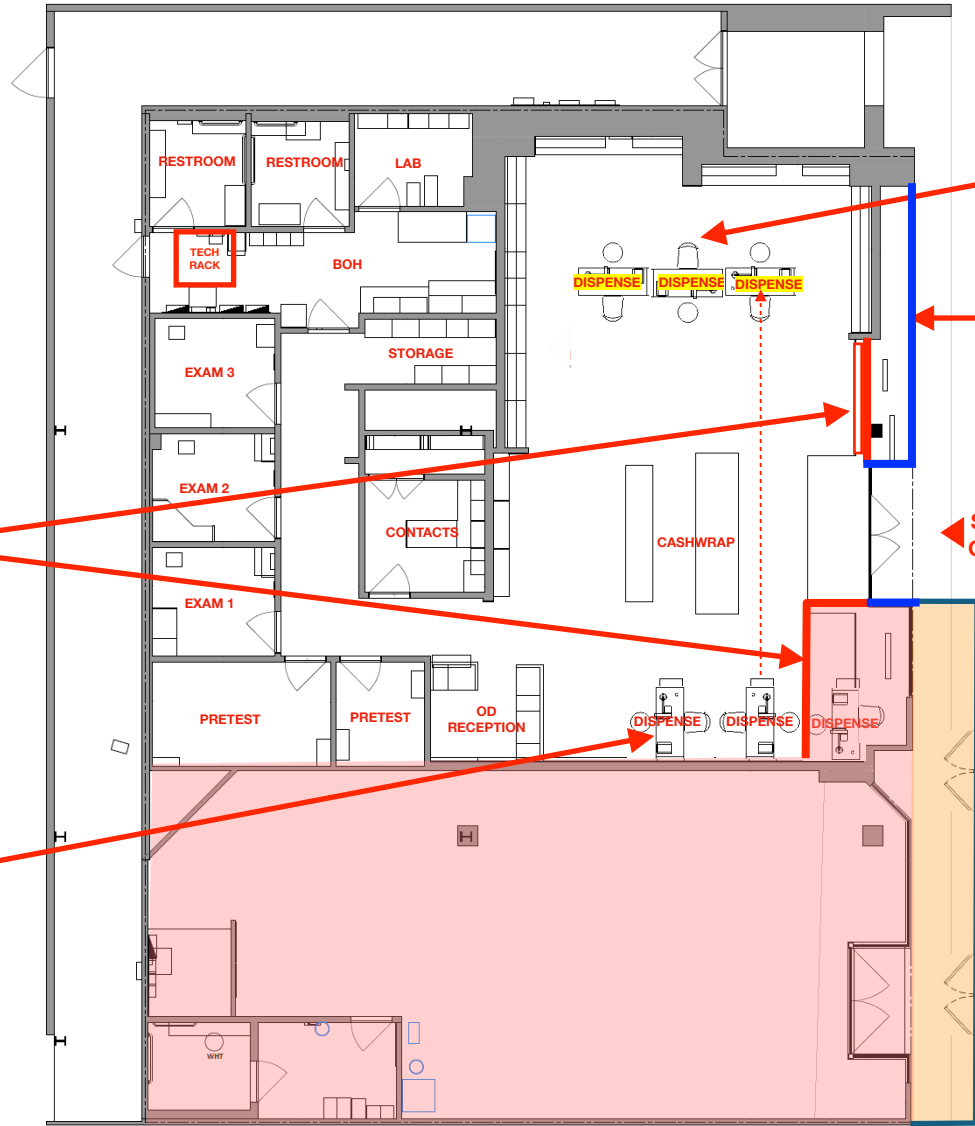


- 3 RELOCATED DISPENSE STATIONS
- 2 IN THIS AREA ALREADY + 1 FROM OTHER SIDE AT DEMISING WALL
- POWER/DATA A MUST

- VINYL GRAPHICS
- OPEN FOR BUSINESS AND ARROWS A MUST

- HARD BARRICADE WITH GRAPHICS
- OPEN FOR BUSINESS AND ARROWS A MUST

LC609 BRIDGEWATER- PHASE 1 FINISH

- PHASE 1 - 5 Weeks
 - PHASE 2 - 6 Weeks
 - PHASE 3 - 4 Weeks
 - PHASE 4 - 4 Weeks (4th Week Dark)
- + SET DOWN - 1 Week
- TOTAL WEEKS 20 (19 + 1)**

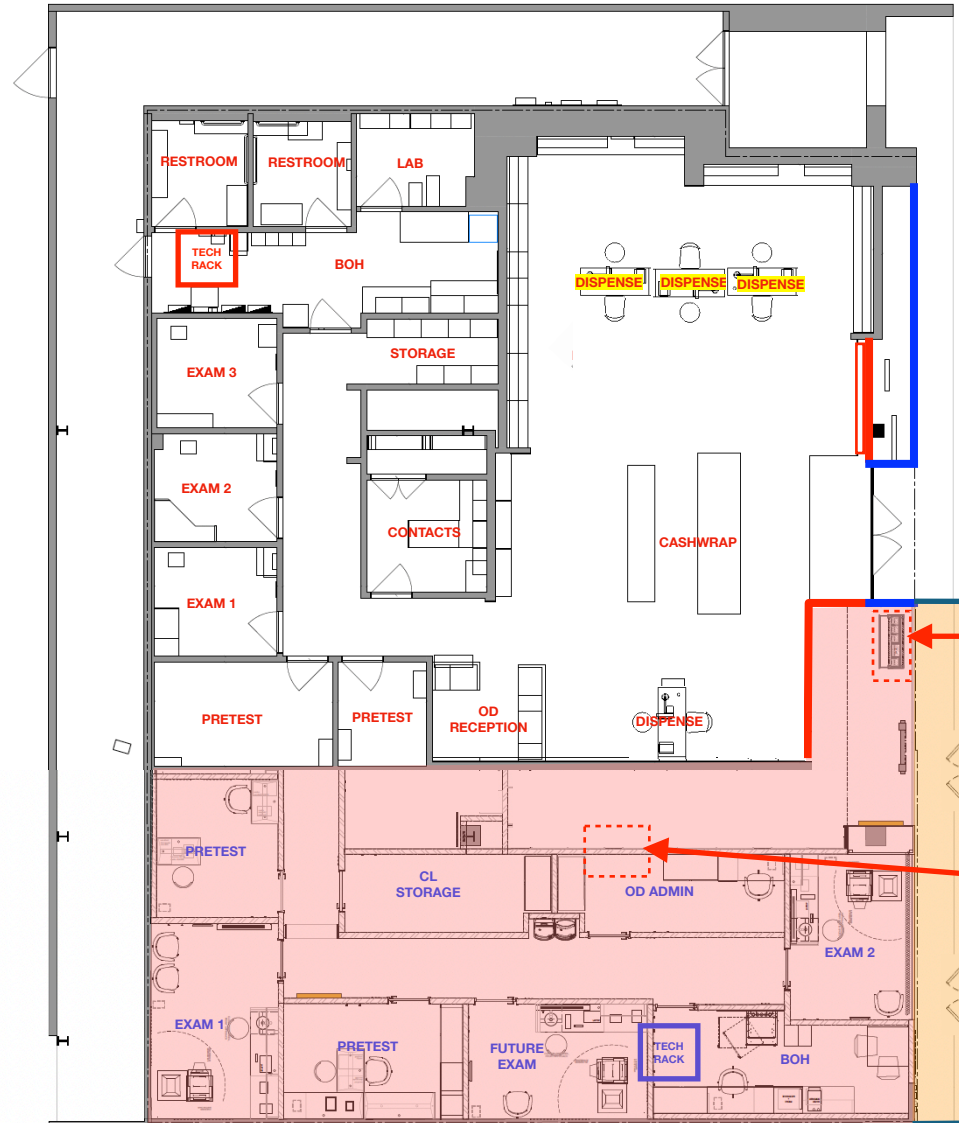


• DO NOT INSTALL CASE TABLE AT WINDOW UNTIL PH4 DARK
• NEED DRYWALL BARRICADE WITH ONE NEW 8' AND ONE NEW 6' SLAT PANELS AT PH3 OPEN
• W/60 ACRYLIC SHELVES 24"L X 6"D EA - A MUST

• CREATE TEMP ACCESS THROUGH OD ADMIN OFFICE WALL INTO COMPLETED PH1 AREA

LC609 BRIDGEWATER- PHASE 2 PREP/CONSTRUCTION

- PHASE 1 - 5 Weeks
- PHASE 2 - 6 Weeks
- PHASE 3 - 4 Weeks
- PHASE 4 - 4 Weeks (4th Week Dark)
- + SET DOWN - 1 Week
- TOTAL WEEKS 20 (19 + 1)**

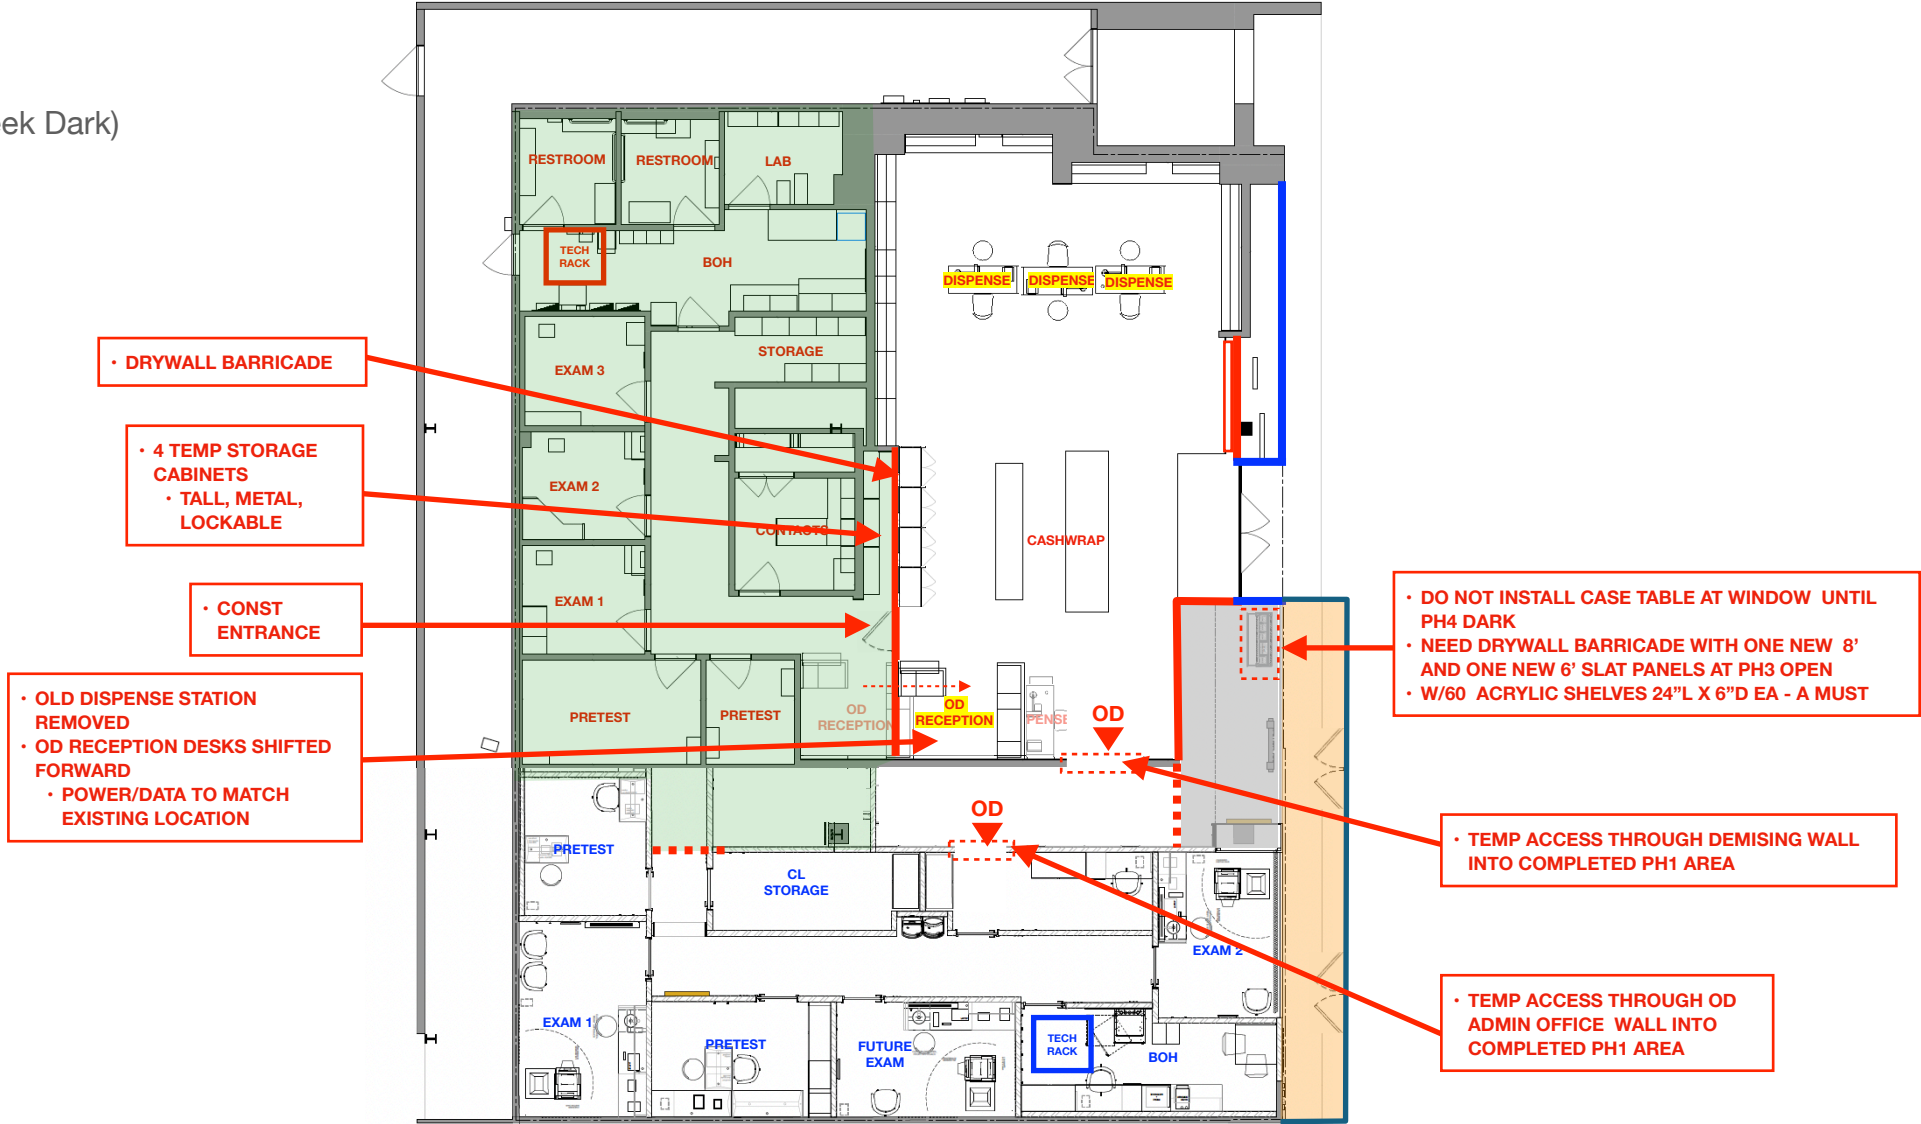

• DRYWALL BARRICADE

• 4 TEMP STORAGE CABINETS
• TALL, METAL, LOCKABLE

• CONST ENTRANCE

• OLD DISPENSE STATION REMOVED
• OD RECEPTION DESKS SHIFTED FORWARD
• POWER/DATA TO MATCH EXISTING LOCATION

• DO NOT INSTALL CASE TABLE AT WINDOW UNTIL PH4 DARK
• NEED DRYWALL BARRICADE WITH ONE NEW 8' AND ONE NEW 6' SLAT PANELS AT PH3 OPEN
• W/60 ACRYLIC SHELVES 24"L X 6"D EA - A MUST


• TEMP ACCESS THROUGH DEMISING WALL INTO COMPLETED PH1 AREA

• TEMP ACCESS THROUGH OD ADMIN OFFICE WALL INTO COMPLETED PH1 AREA

LC609 BRIDGEWATER- PHASE 2 FINISH

- PHASE 1 - 5 Weeks
 - PHASE 2 - 6 Weeks**
 - PHASE 3 - 4 Weeks
 - PHASE 4 - 4 Weeks (4th Week Dark)
- + SET DOWN - 1 Week
- TOTAL WEEKS 20 (19 + 1)**


• PORTION OF MILLWORK REMOVED AND DEMO WALL AT RETAIL TO CREATE ACCESS TO BE COMPLETED AT PH2 OPEN/PH 3 START

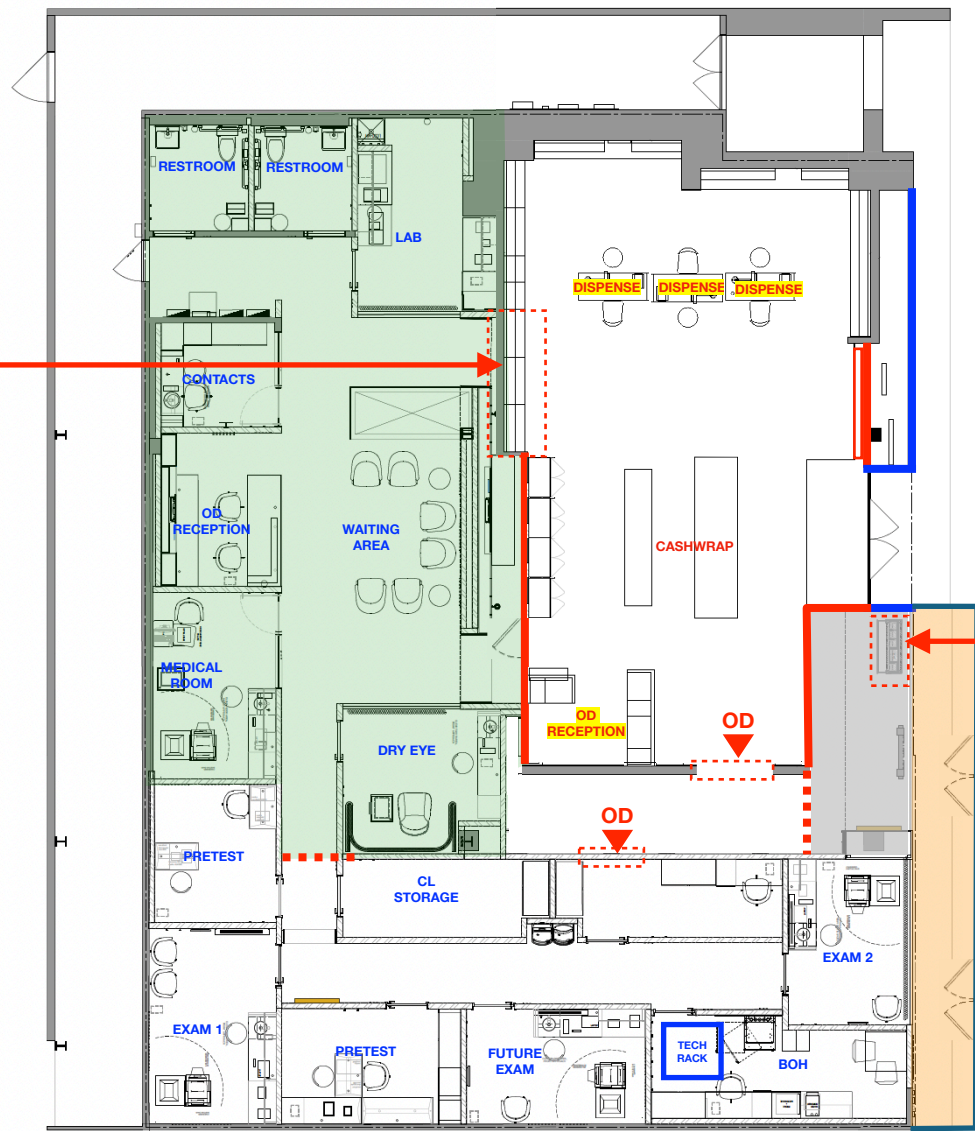

• DO NOT INSTALL CASE TABLE AT WINDOW UNTIL PH4 DARK
• NEED DRYWALL BARRICADE WITH ONE NEW 8' AND ONE NEW 6' SLAT PANELS AT PH3 OPEN
• W/60 ACRYLIC SHELVES 24"L X 6"D EA - A MUST

LC609 BRIDGEWATER- PHASE 3 PREP/CONSTRUCTION

- PHASE 1 - 5 Weeks
- PHASE 2 - 6 Weeks
- PHASE 3 - 4 Weeks**
- PHASE 4 - 4 Weeks (4th Week Dark)
- + SET DOWN - 1 Week
- TOTAL WEEKS 20 (19 + 1)**

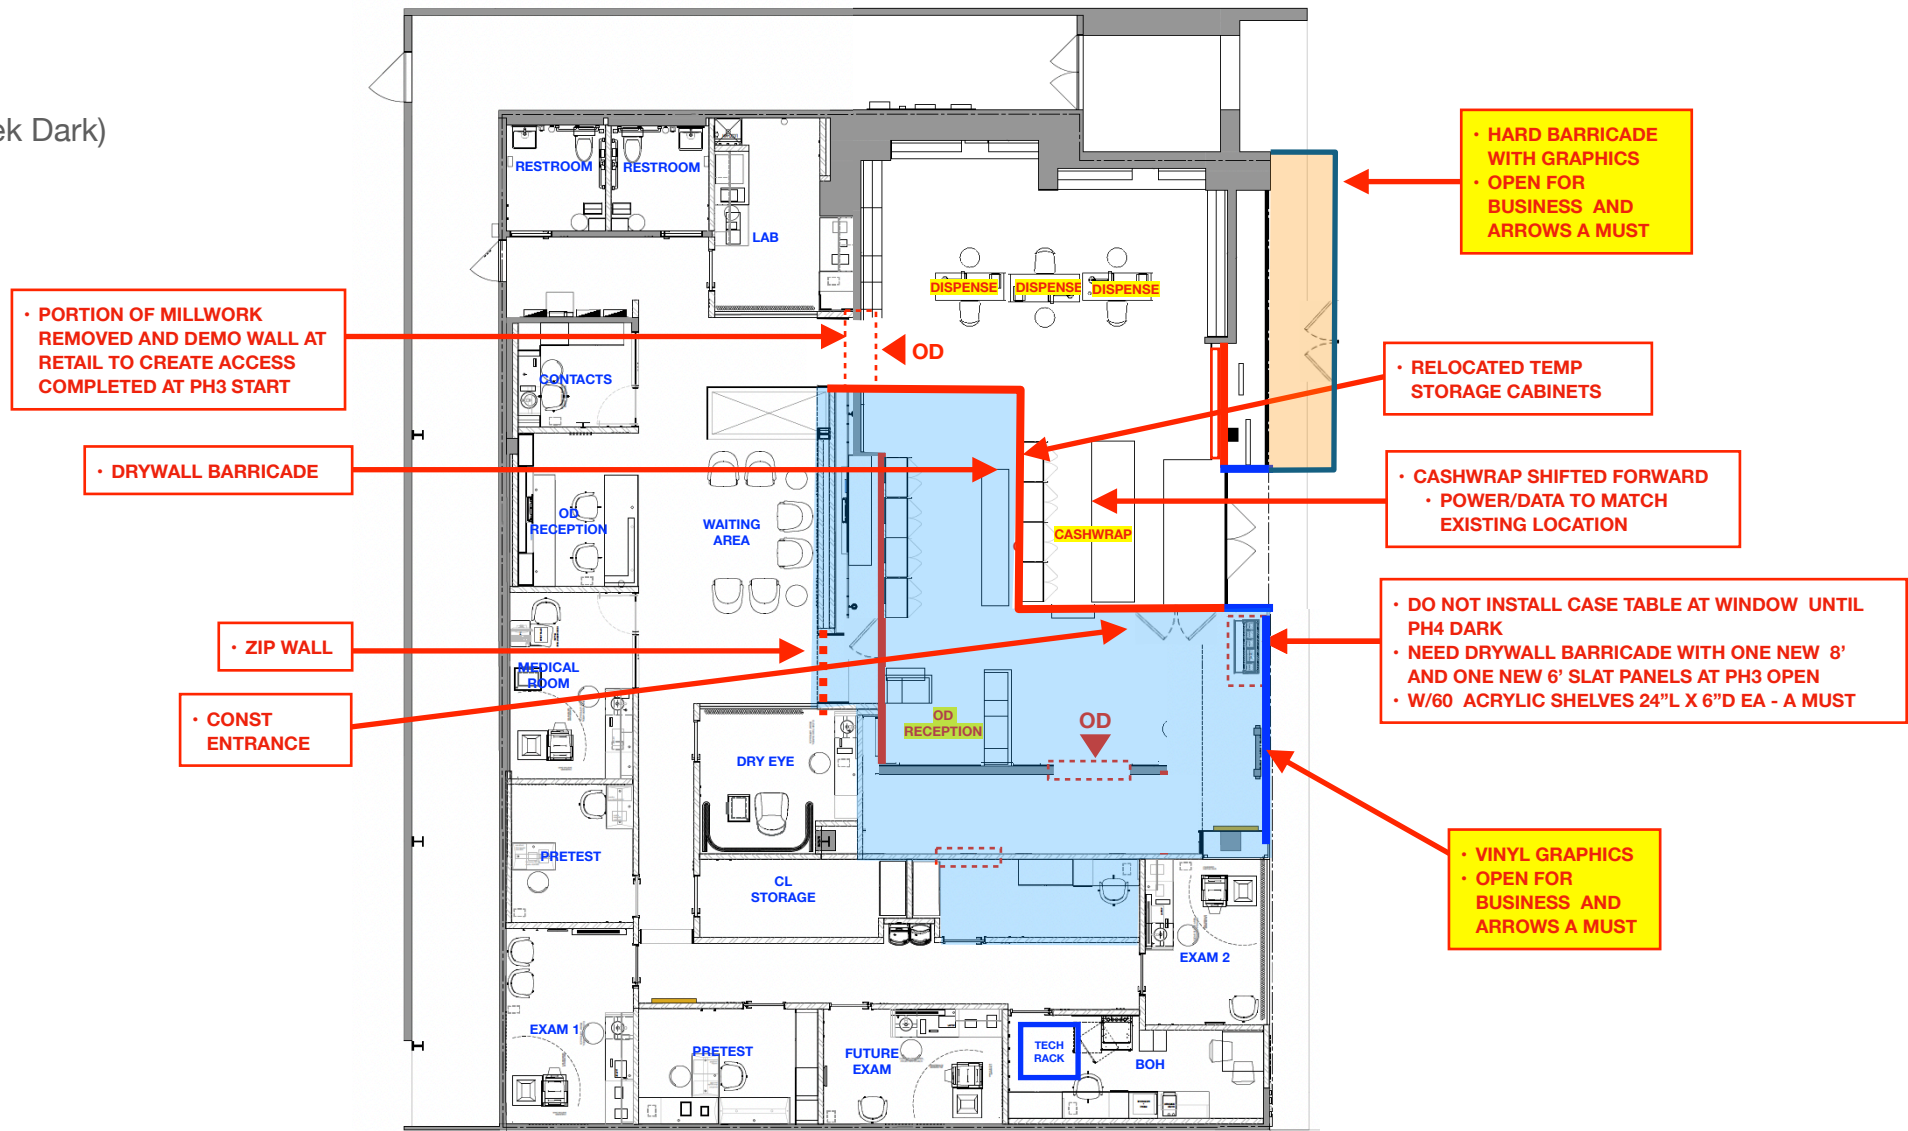

• PORTION OF MILLWORK REMOVED AND DEMO WALL AT RETAIL TO CREATE ACCESS COMPLETED AT PH3 START

• DRYWALL BARRICADE

• ZIP WALL

• CONST ENTRANCE

• HARD BARRICADE WITH GRAPHICS
• OPEN FOR BUSINESS AND ARROWS A MUST

• RELOCATED TEMP STORAGE CABINETS


• CASHWRAP SHIFTED FORWARD
• POWER/DATA TO MATCH EXISTING LOCATION

• DO NOT INSTALL CASE TABLE AT WINDOW UNTIL PH4 DARK
• NEED DRYWALL BARRICADE WITH ONE NEW 8' AND ONE NEW 6' SLAT PANELS AT PH3 OPEN
• W/60 ACRYLIC SHELVES 24"L X 6"D EA - A MUST

• VINYL GRAPHICS
• OPEN FOR BUSINESS AND ARROWS A MUST

LC609 BRIDGEWATER- PHASE 3 FINISH

- PHASE 1 - 5 Weeks
 - PHASE 2 - 6 Weeks
 - PHASE 3 - 4 Weeks**
 - PHASE 4 - 4 Weeks (4th Week Dark)
- + SET DOWN - 1 Week
- TOTAL WEEKS 20 (19 + 1)**

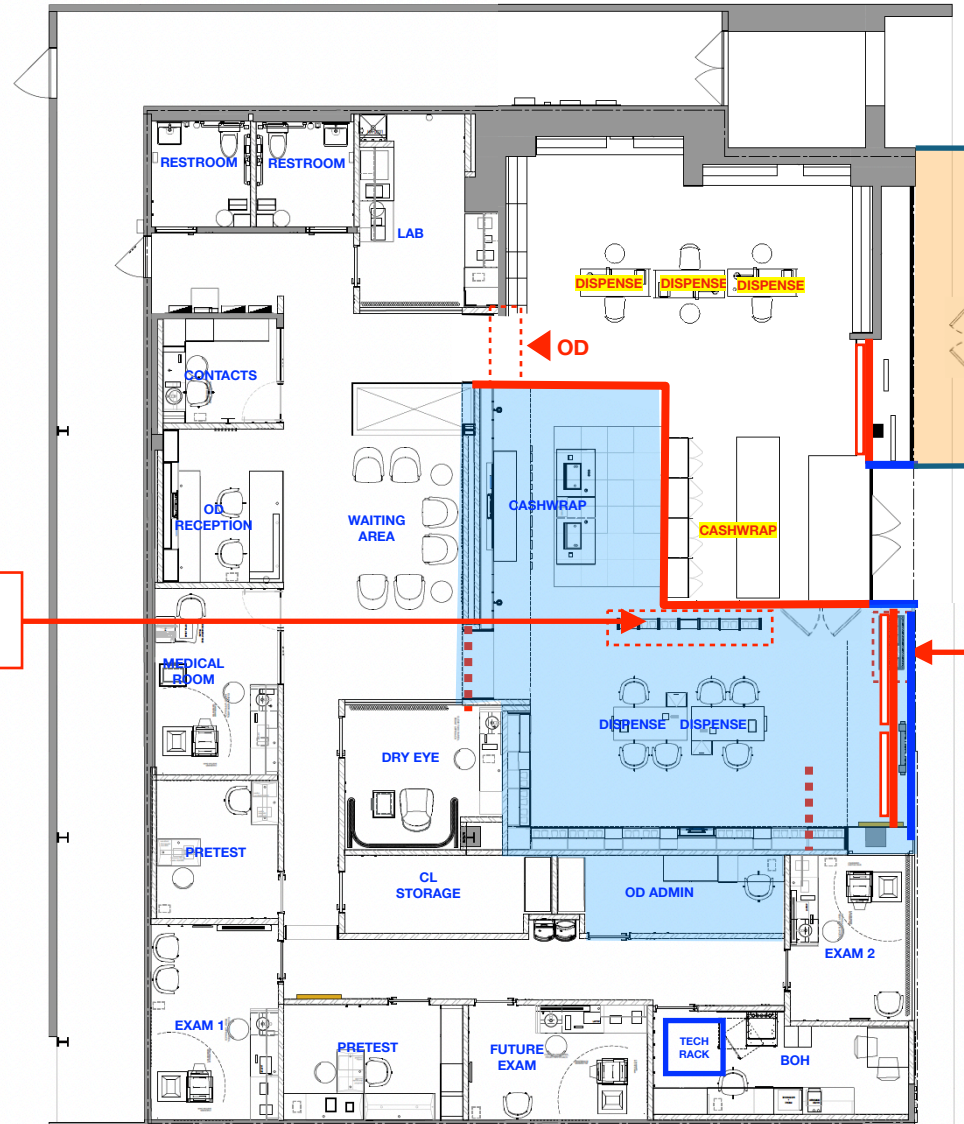

• DO NOT INSTALL SEE-THROUGH FIXTURES UNTIL PH4 DARK PERIOD TO ALLOW FOR BARRICADE/ SLAT PANELS SHIFT AT PH3 OPEN/PH4 START


• DO NOT INSTALL CASE TABLE AT WINDOW UNTIL PH4 DARK
• NEED DRYWALL BARRICADE WITH ONE NEW 8' AND ONE NEW 6' SLAT PANELS AT PH3 OPEN
• W/60 ACRYLIC SHELVES 24"L X 6"D EA - A MUST

LC609 BRIDGEWATER- PHASE 4 PREP/CONSTRUCTION

- PHASE 1 - 5 Weeks
- PHASE 2 - 6 Weeks
- PHASE 3 - 4 Weeks
- PHASE 4 - 4 Weeks (4th Week Dark)**

+ SET DOWN - 1 Week

TOTAL WEEKS 20 (19 + 1)

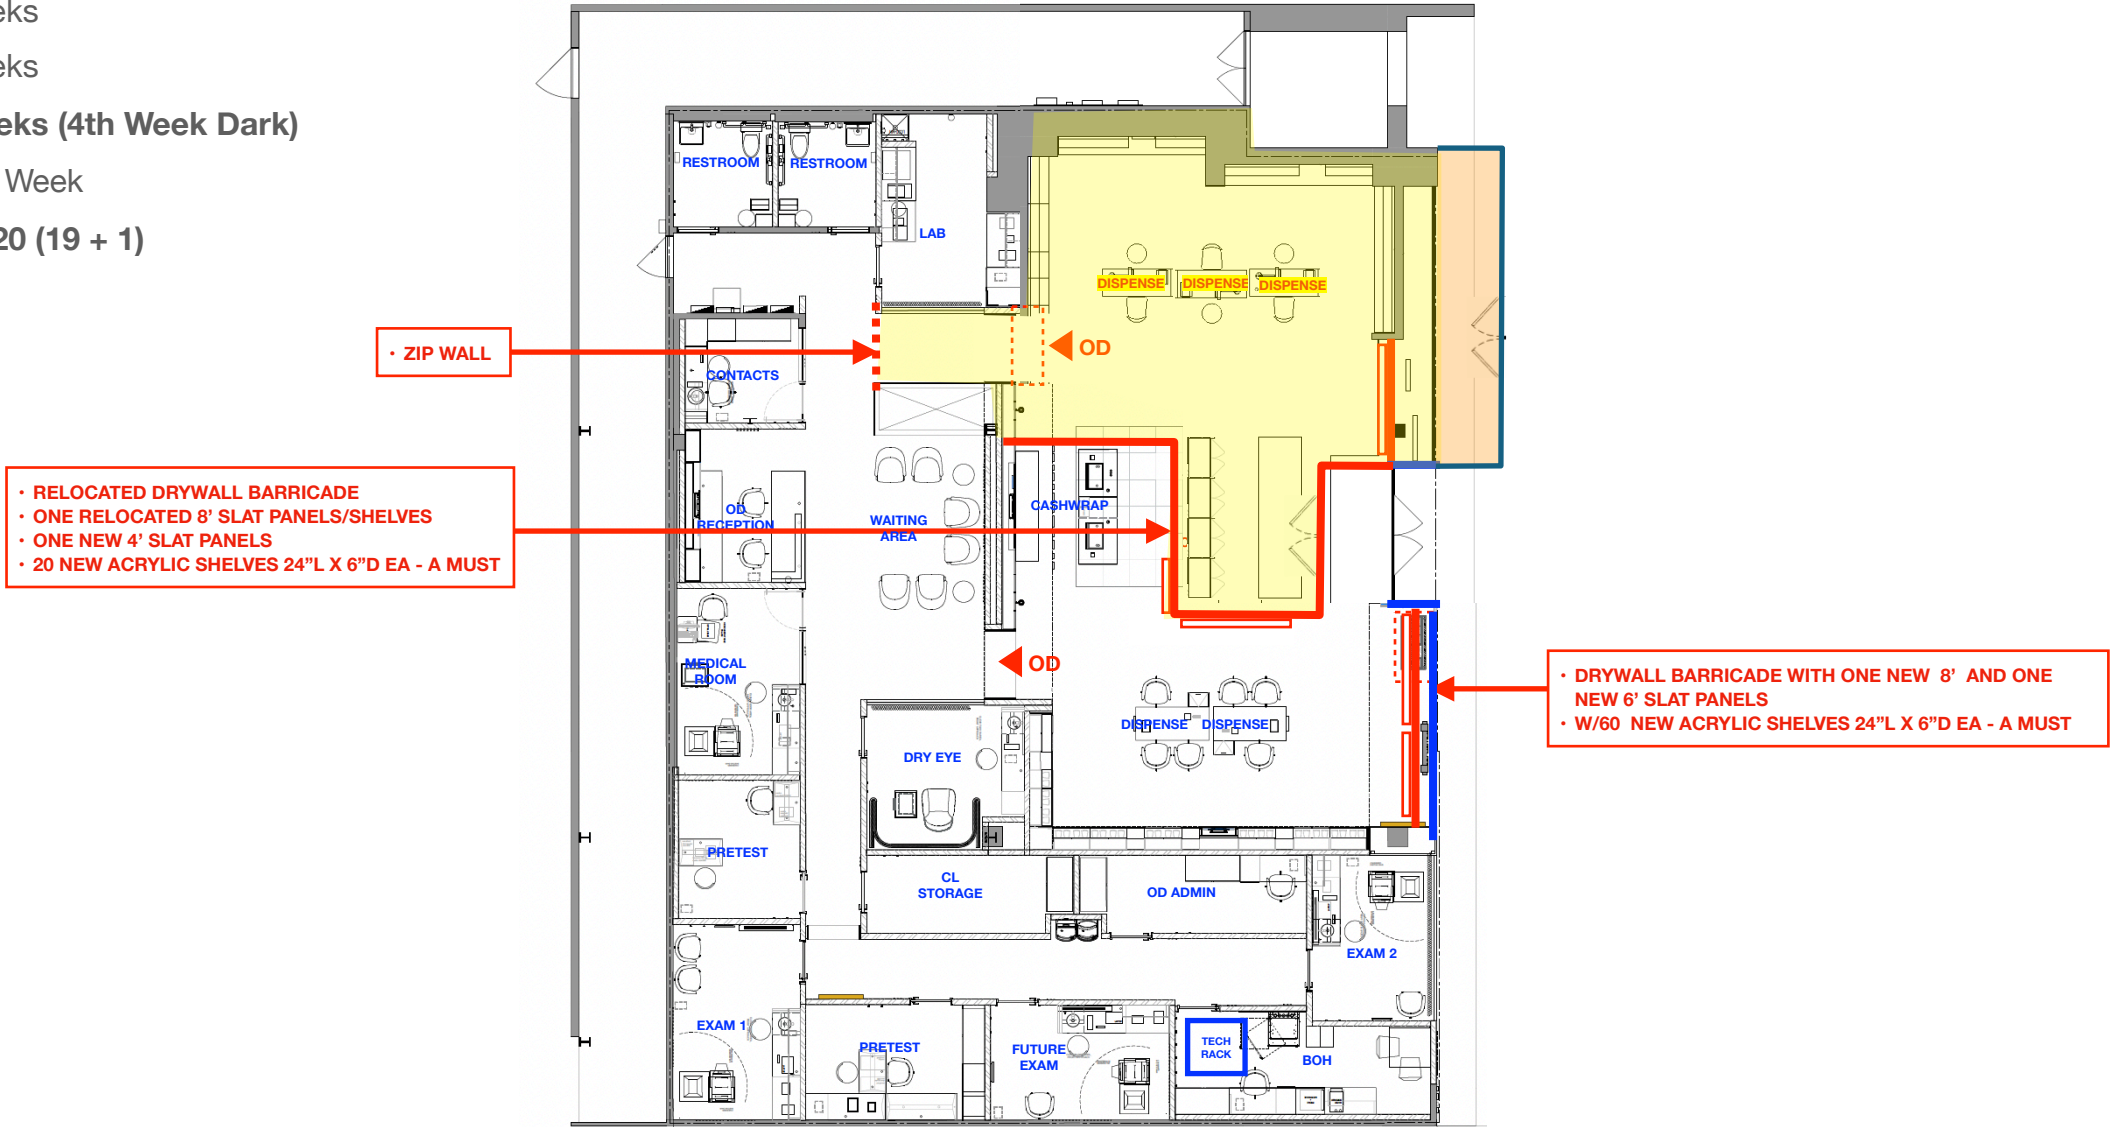


LC609 BRIDGEWATER- PHASE 4 FINISH

- PHASE 1 - 5 Weeks
- PHASE 2 - 6 Weeks
- PHASE 3 - 4 Weeks
- PHASE 4 - 4 Weeks (4th Week Dark)**

+ SET DOWN - 1 Week

TOTAL WEEKS 20 (19 + 1)

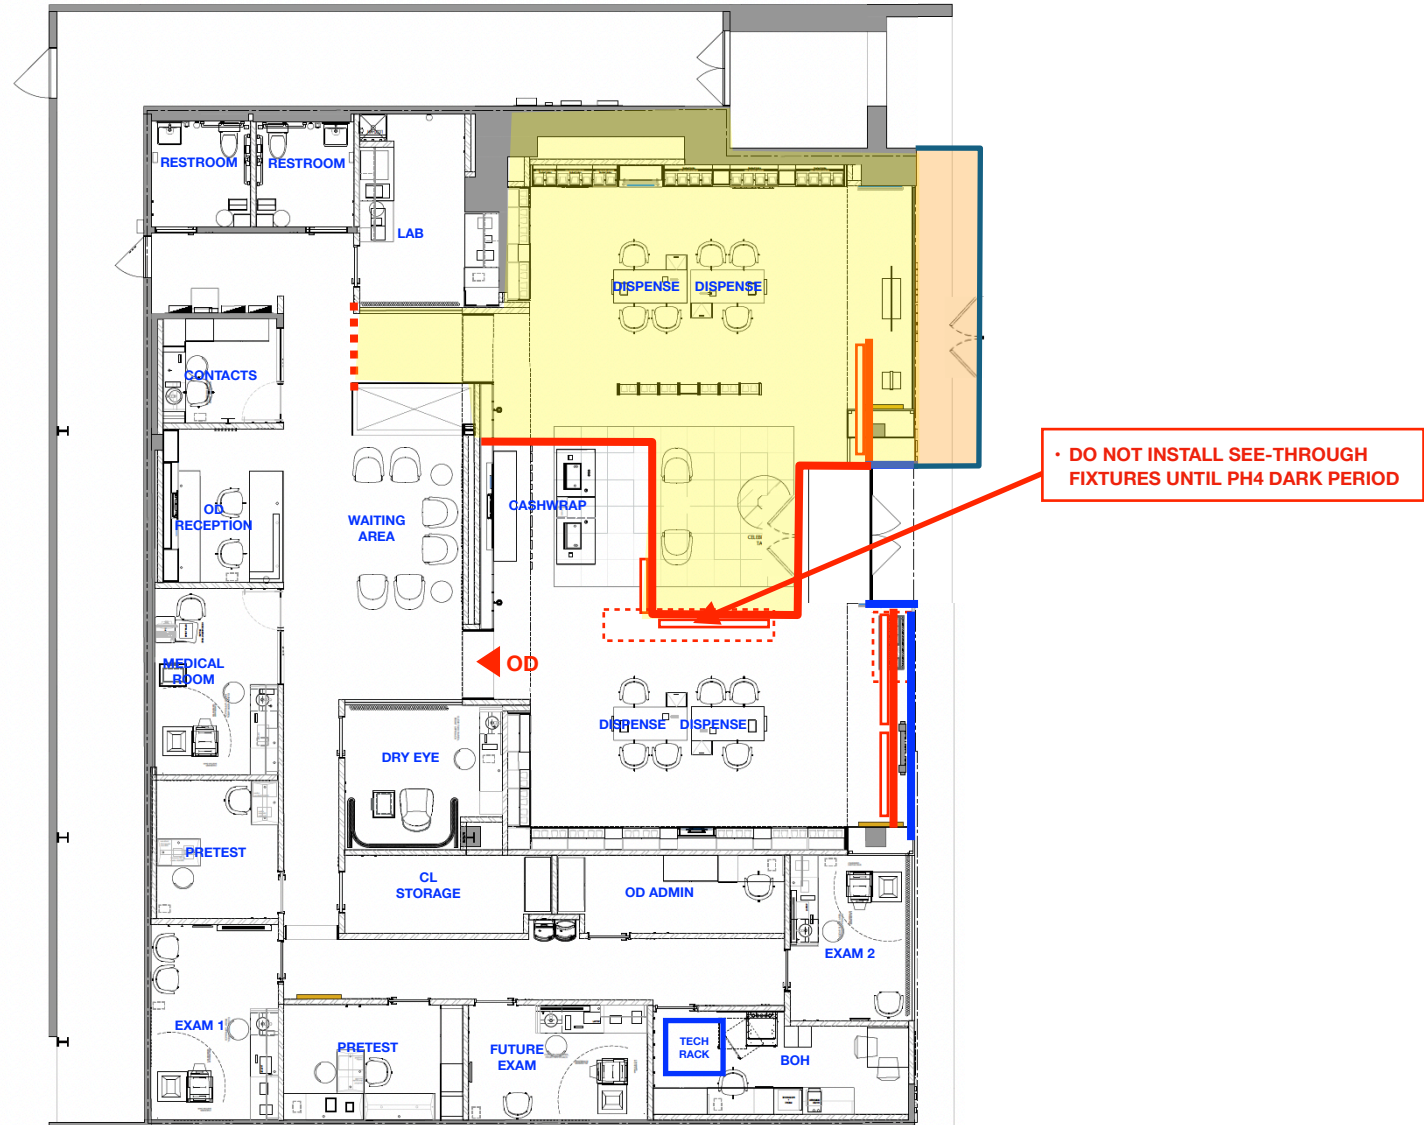

LC609 BRIDGEWATER- PHASE 4 DARK CONSTRUCTION

- PHASE 1 - 5 Weeks
- PHASE 2 - 6 Weeks
- PHASE 3 - 4 Weeks
- PHASE 4 - 4 Weeks (4th Week Dark)**

+ SET DOWN - 1 Week

TOTAL WEEKS 20 (19 + 1)




• CLADDING AT STOREFRONT DURING DARK WEEK?

LC609 BRIDGEWATER- PHASE 4 DARK FINISH

- PHASE 1 - 5 Weeks
- PHASE 2 - 6 Weeks
- PHASE 3 - 4 Weeks
- PHASE 4 - 4 Weeks (4th Week Dark)**

+ SET DOWN - 1 Week

TOTAL WEEKS 20 (19 + 1)

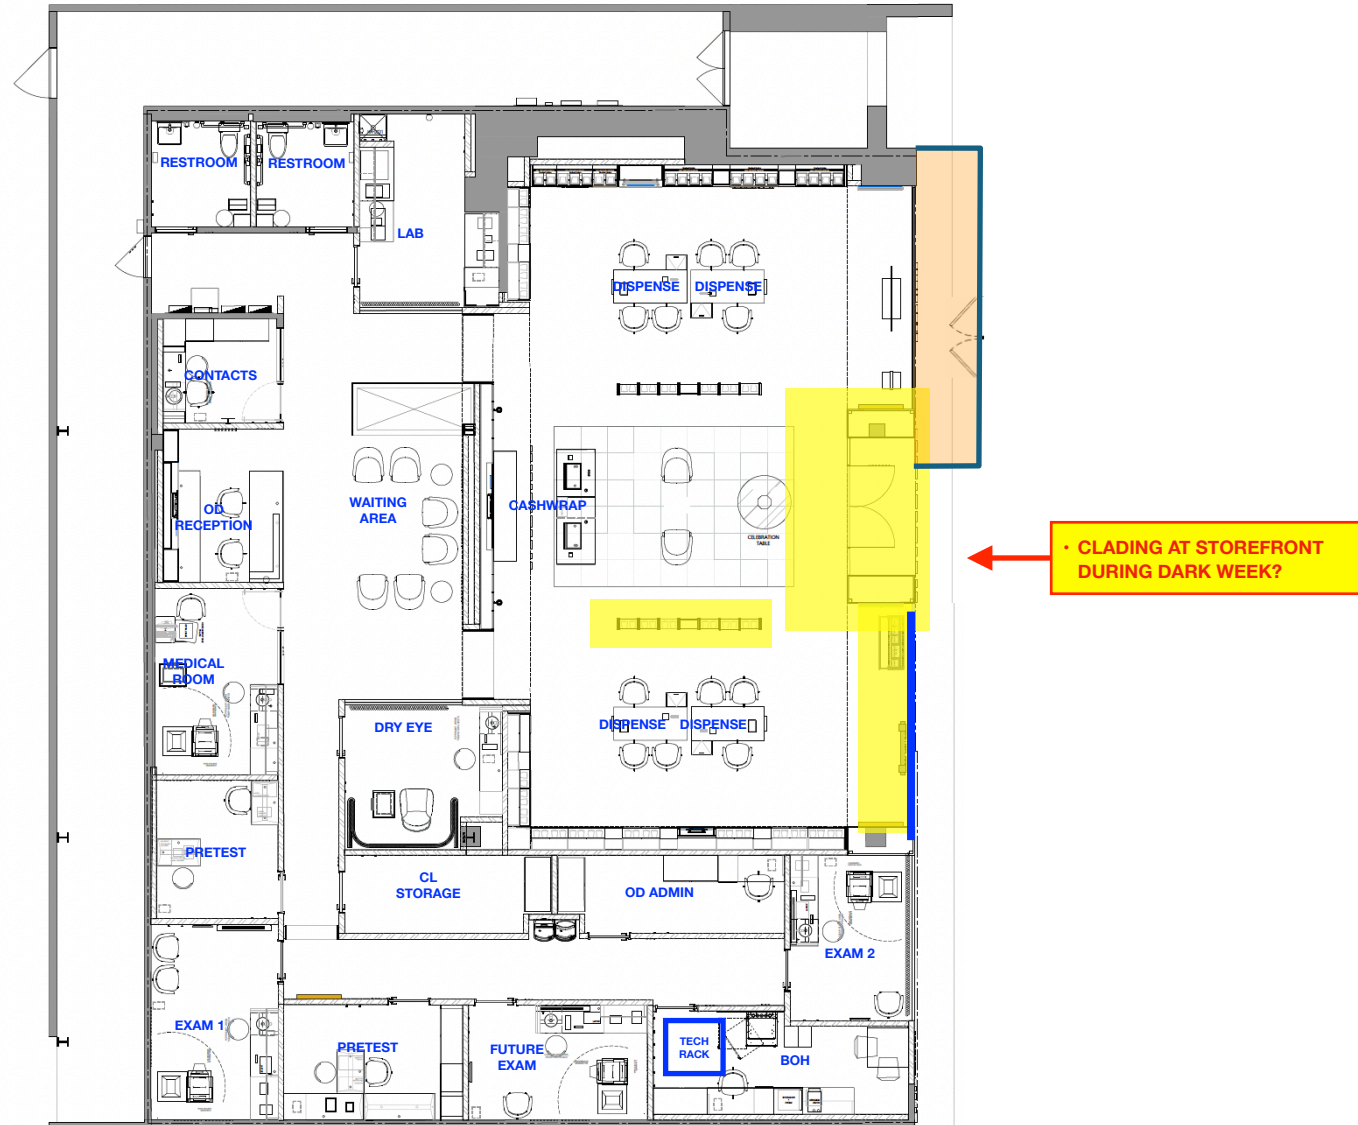

LC609 BRIDGEWATER- FINAL LAYOUT

- PHASE 1 - 5 Weeks
- PHASE 2 - 6 Weeks
- PHASE 3 - 4 Weeks
- PHASE 4 - 4 Weeks (4th Week Dark)

+ SET DOWN - 1 Week

TOTAL WEEKS 20 (19 + 1)

